

**OHM Remediation  
Services Corp.**

A Subsidiary of OHM Corporation

September 18, 1996

Ms. Kate Landman  
Atlantic Division Code 18232  
Naval Facilities Engineering Command  
1510 Gilbert Street  
Norfolk, VA 23511-2699

Re: Contractor's Closeout Report  
Site 41, MCAS New River  
Contract N62470-93-D-3032; Delivery Order 0101  
MCB Camp Lejeune, NC

Dear Ms. Landman:

Submitted for your review and approval is this letter Closeout Report for D.O. 0101, Site 41, MCAS New River, MCB Camp Lejeune, N.C.

**Overview**

OHM installed fencing and signs in support of D.O. 0101 to restrict access to Site 41 at the Marine Corps Air Station. Site access was required to be restricted because Site 41 was previously used as an open burn dump from 1946 to 1970. In addition to construction debris and several other types of waste, it is reported that in the mid-1960s, at least two waste disposal incidents occurred involving the disposal of drummed wastes from trucks. These wastes were described as being similar to the types of wastes disposed of at Site 69 (Rifle Range Chemical Dump).

**Field Activities**

OHM commenced field activities on August 8, 1996 and completed the field work on August 15, 1996. A photo log is attached documenting the work performed.

OHM installed 150 feet of fencing with twin 10 feet wide swing gates across a dirt road at the southeast access to the site. At the west access via the same road OHM installed 50 feet of fence with a 16 feet swing gate. Figure 1 identifies the as built locations of the fencing and gates.

Thirty four 24 inches by 24 inches metallic signs were installed around the east, west and southern boundaries of the site. These signs were posted on existing trees and adjacent to the two gates. The signs have a yellow background with red lettering. Figure 1 also indicates the locations of the signs.

### **Health & Safety Issues**

The project was completed safely without any accidents or near misses.

### **Schedule Impacts/Changes**


The project was delayed awaiting final approval from the New River Air Station of the sign wording and locations. The signs were changed from a green background with white lettering to a yellow background with red lettering. The final wording on the signs is as follows:

**KEEP OUT  
HAZARDOUS  
WASTE  
SITE**

Additional signs were installed to encompass the southern boundary of the site (34 versus 15).

The final inspection and approval of the site was conducted with the ROICC on September 18, 1996.

Very truly yours,  
**OHM Remediation Services, Inc.**



James A. Dunn, Jr., P.E.  
Senior Project Manager

### **Attachments**



- I. Photo Log
- II. Figure 1

pc: See Page 3

Page 3

Closeout Report, Site 41

pc: Neal Paul - IRD/EMD w/enclosures (2)  
Lt. Hansen - ROICC w/enclosures  
Matt Bartman - Baker Environmental w/enclosures  
Dave Lown - NCDEHNR w/enclosures  
John Franz - OHM w/enclosures  
Jerry Haste - NAVFACENGCOM w/enclosures  
Gena Townsend - EPA Region IV w/enclosures  
OHM Project File/18421 w/enclosures  
Dwayne Currie - OHM w/enclosures  
Greg Gilles - OHM w/enclosures  
Chuck Lawrence - Stone & Webster w/enclosures  
Project File 18421-14.3 w/enclosures

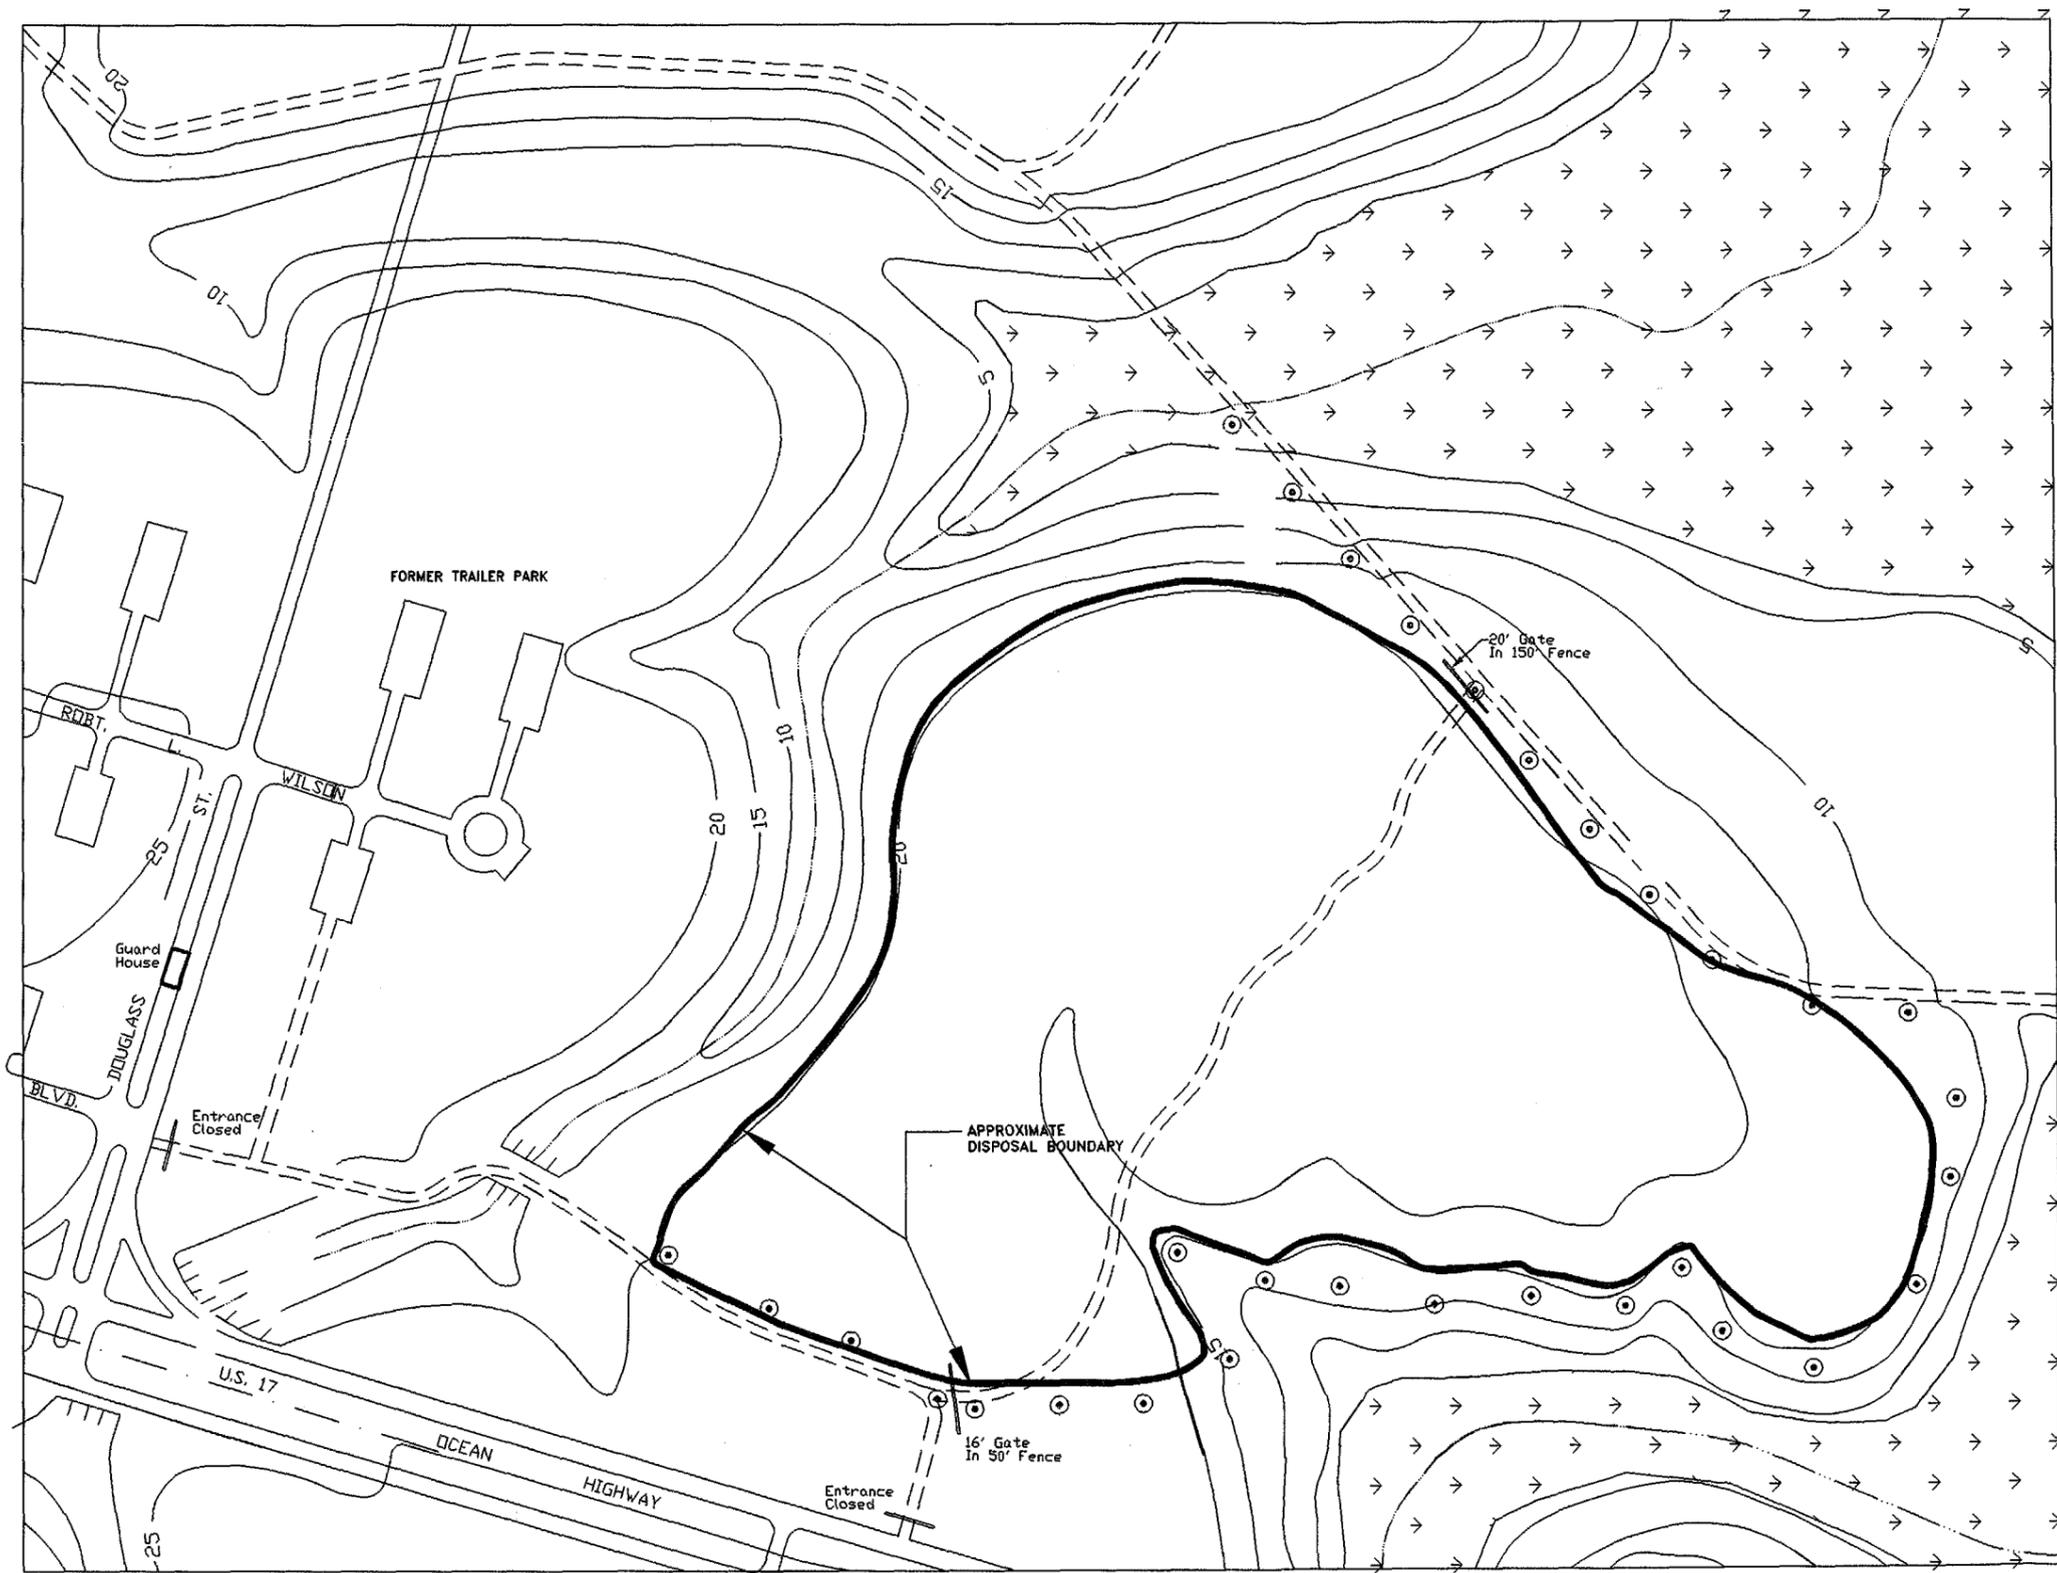

**LEGEND**

- MARSH
- TOPOGRAPHIC ELEVATION LINES (FEET, MEAN SEA LEVEL)
- ROAD (IMPROVED)
- ROAD (UNIMPROVED)
- INTERMITTENT STREAM
- SIGN @ 200' O.C. INSTALLED ON GATES OR EXISTING TREES

SOURCE: LANTDIV, OCT. 1991, BAKER 1996

OHM Remediation Services Corp. NORCROSS, GEORGIA A SUBSIDIARY OF OHM CORPORATION		
DRAWN BY	J. LANGE	3/15/96
CHECKED BY	J. DUNN	3/15/96
APPROVED BY	-	DATE
REV. 0	SHEET # -	PROJECT NO. 18421

**FIGURE 2**  
**AS BUILT**  
**GENERAL ARRANGEMENT MAP**  
**SITE 4I-CAMP GEIGER DUMP**  
 D.O. 101  
 MCB CAMP LELEUNE  
 PREPARED FOR  
 LANTDIV

01808 II 012

D:\OHM\LANTDIV\LELEUNE\18421\F162.DWG



**Project No. 18421**                      **Date: 8/14/96**  
**Contract No. N62470-93-D-3032**  
**Delivery Order: 101**  
**Description: 150-foot section of fence with 20-foot gate on the east end of the spine road**



**Project No. 18421**                      **Date: 8/14/96**  
**Contract No. N62470-93-D-3032**  
**Delivery Order: 101**  
**Description: 50 foot section of fence with 20 foot gate on the west end of the spine road**

01808 IIBIY



**Project No. 18421**                      **Date: 8/14/96**  
**Contract No. N62470-93-D-3032**  
**Delivery Order: 101**  
**Description: Warning sign posted at 200 foot intervals**  
**around the southern end**



**Project No. 18421**                      **Date: 8/14/96**  
**Contract No. N62470-93-D-3032**  
**Delivery Order: 101**  
**Description: Warning sign posted on the gate of the west**  
**end of the spine road**



**Project No. 18421**                      **Date: 8/14/96**  
**Contract No. N62470-93-D-3032**  
**Delivery Order: 101**  
**Description: Warning sign posted on the gate of the east  
end of the spine road**
