



DEPARTMENT OF THE NAVY

SOUTHERN DIVISION

NAVAL FACILITIES ENGINEERING COMMAND

2155 EAGLE DR. P O BOX 10068

CHARLESTON S. C. 29411-0068

32501.003

03.01.03.0001

PLEASE ADDRESS REPLY TO THE
COMMANDING OFFICER, NOT TO
THE SIGNER OF THIS LETTER.

5090/11

Code 18211

03 JUN 1991

CERTIFIED MAIL- REQUEST RETURN RECEIPT

Ms. Allison Drew
Environmental Protection Agency
Region IV
Waste Management Division
RCRA and Federal Facilities Branch
345 Courtland Street
Atlanta, Georgia 30365

N00204.AR.000227

NAS PENSACOLA

5090.3a

Subj: PROJECT SCHEDULE FOR BATCH 2: GROUPS F, G, J, K, M, AND N
(SITES 9, 10, 23, 29, 34, 25, 27, 3, 19, 7, 20, 21, 31, AND
36) AND SAMPLING SCHEDULES: CONTAMINATION ASSESSMENT/REMEDIAL
ACTIVITIES INVESTIGATIONS, NAVAL AIR STATION (NAS) PENSACOLA,
FLORIDA.

Dear Ms. Drew:

We have enclosed the subject project schedule status for the following project-related activities which have occurred and are yet to occur:

- the aerial photograph and existing data analysis task- completed at all 12 sites.
- the site reconnaissance task- completed at all 12 sites.
- the existing well evaluation and resampling task was initiated for sites 3, 9, 23, 29, 31, and 34. However, due to a prolonged period of rainy weather, this task was not completed as of the end of April.
- the habitat/biota survey task was initiated and completed for all sites except sites 25, and 27.
- the grid establishment and surface emissions survey task was initiated for all sites; and
- the utilities survey task was initiated for sites 3, 7, 21, and 36.

As shown on enclosure (1), the principal activities scheduled to occur during the following months are: the completion of the existing well evaluation and resampling task; the completion of the grid establishment and surface emission task; the initiation and completion of the radiation survey task; the initiation of the geophysical survey tasks; continuation of the utilities survey


Subj: PROJECT SCHEDULE FOR BATCH 2: GROUPS **F, G, J, K, M, AND N**
(SITES **9, 10, 23, 29, 34, 25, 27, 3, 19, 7, 20, 21, 31, AND 36**) AND SAMPLING SCHEDULES: CONTAMINATION ASSESSMENT/REMEDIAL
ACTIVITIES INVESTIGATIONS, NAVAL AIR STATION (NAS) PENSACOLA,
FLORIDA.

task; the initiation of the soil gas and headspace tasks; and the submittal of the draft data management plan. The only significant changes to the project schedule from previous month are: moving the temporary well installation and sampling task, the hydrologic assessment task, and the sediment sampling task each (especially at sites 25, and **27**- Group G) ahead one week to begin as early as June 18, and no later than June **24**. **As** for other groups, sampling will begin on July **1**, and August **5, 1991**, respectively. **So** far, there are no other anticipated changes to the project schedules for this work.

Per the Federal Facilities Agreement (FFA) Section XV. B : Sampling and Data Availability, we are notifying you in advance of soil sampling collections to occur as early as June **18**, and no later than June **24, 1991** at Groups F and G (Sites **9, 10, 23, 29, 34, 25, and 27**). Please notify **us** as soon as possible, if you plan to collect samples.

Please contact Ms. Suzanne O. Sanborn (Code 18211) at **(803) 743-0574**, if you should have any questions concerning the project schedule.

Sincerely,




MR. J.B. MALONE, JR., P.E.
MANAGER OF THE INSTALLATION
RESTORATION, EAST SECTION

Encl:

(1) Project Schedule for subject

copy to:

NAS Pensacola (Mr. Ron Joyner, Code 18520) w/encl
FDER (Mr. Eric Nuzie) w/out encl

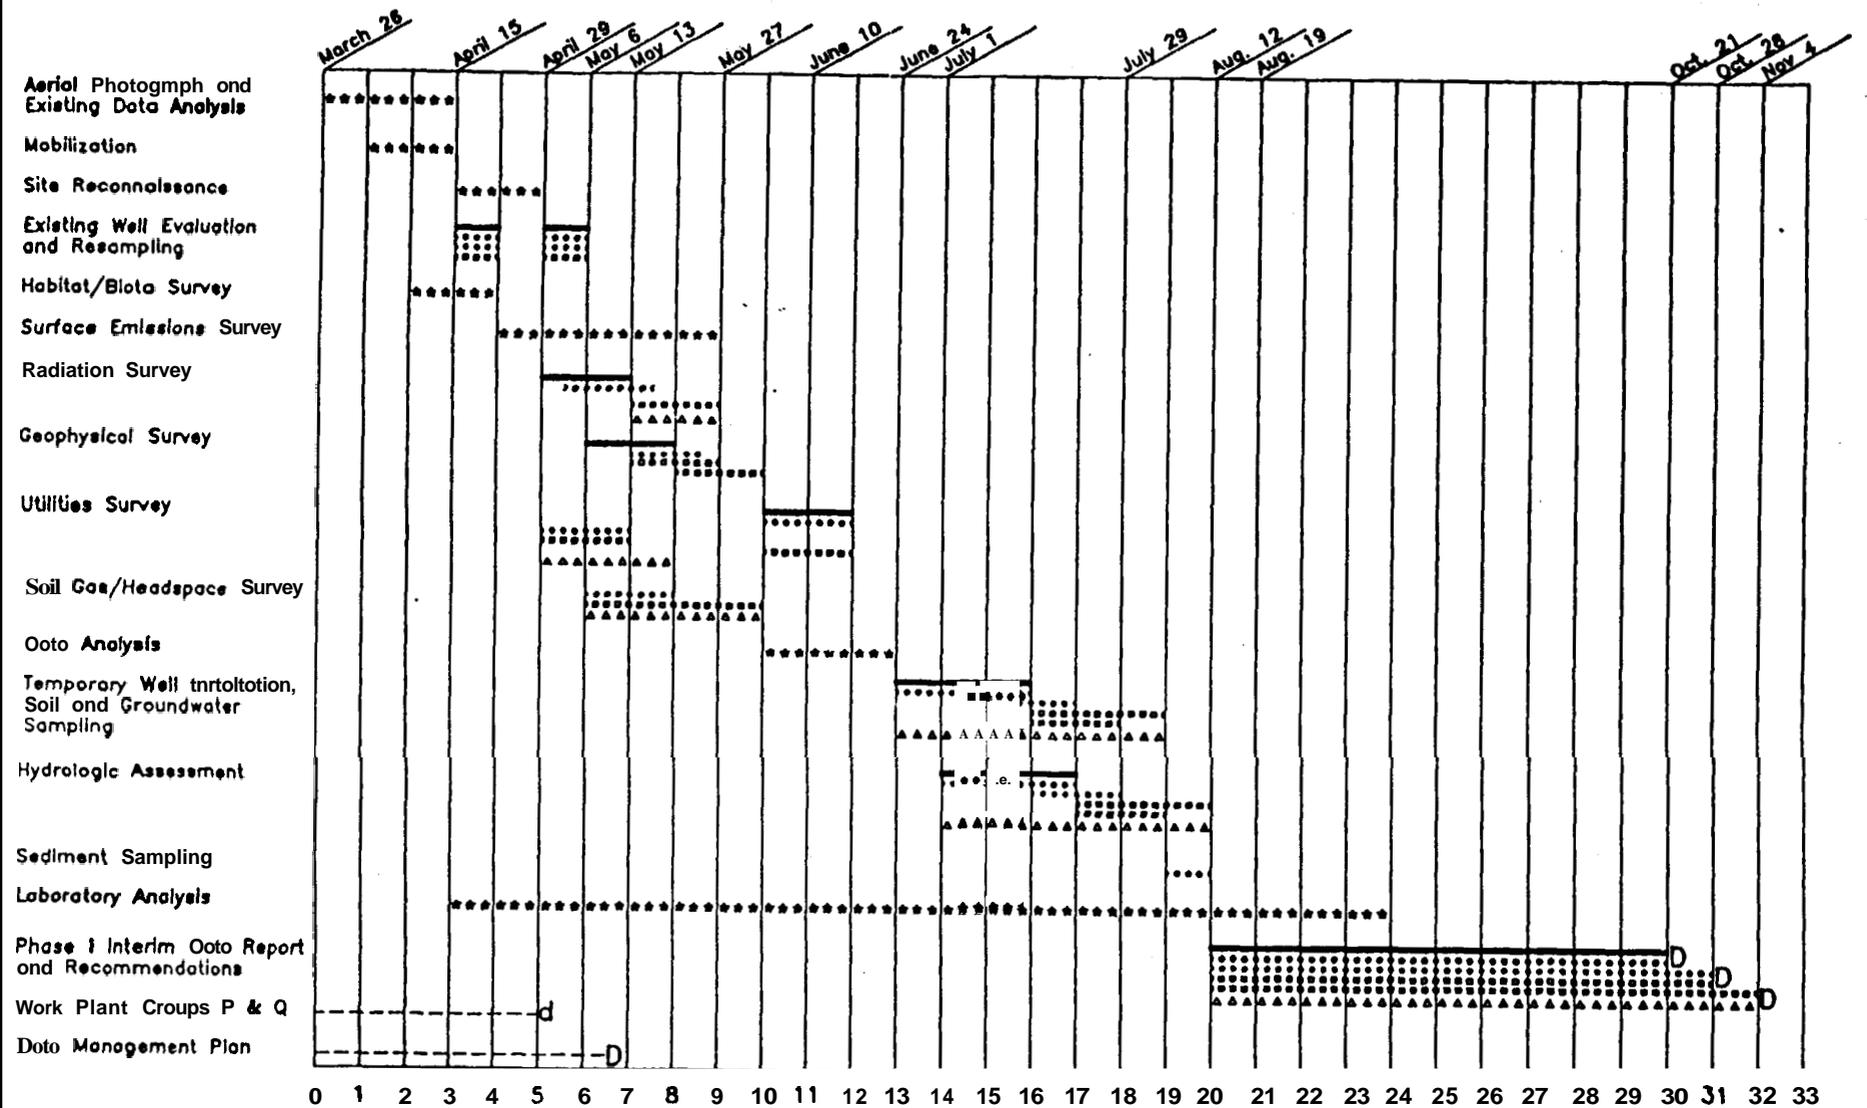

KEY:

—	Group F	□□□	Group K	***	ALL GROUPS
...	Group G	me=	Group M	d	~ 0 Draft to N
...	Group J	▲▲▲	Group N	D	90% Draft to Navy

Attachment B
 COMBINED SCHEDULE FOR PHASE I BATCH 2 SITES FIELDWORK AND REPORTS,
 GROUPS P & Q WORK PLP AND DATA MANAGEMENT PLAN
 NAS ACOLA

E7 re (1)
