

N00204.AR.005389
NAS PENSACOLA
5090.3a

TECHNICAL MEMORANDUM REGARDING EXTENSION OF CALENDAR YEAR 2012 SITE
MANAGEMENT PLAN DEADLINES EXTENSION NUMBER 2015-01 NAS PENSACOLA FL
01/09/2015
NAVFAC SOUTHERN



DEPARTMENT OF THE NAVY
Naval Facilities Engineering Command Southeast
Jacksonville, FL 32212-0030

Memorandum for the file

Date: January 9, 2015

Subject: Extension of Calendar Year 2012 NAS Pensacola Site Management Plan (SMP) Deadlines, Extension Number 2015-001.

From: Patty Marajh-Whitemore, Navy
David Grabka, FDEP
Tim Woolheater, USEPA Region 4

To: File

In accordance with Part XXIII of the October 23, 1990, Federal Facilities Agreement, deadlines established in the SMP may be extended pursuant to part XXIV. Below is a request for extending a deadline date in accordance with Part XXIV, paragraph A.1-4 as agreed to by the parties and is extended in accordance with paragraph E. The change recorded in this memo will be reflected in the calendar year (CY) 2015 Final SMP update submitted December 1, 2014.

1. **OU/site number & description :** OU 19, Site 44 – Former UST Site 3221
2. **Deadline or schedule being extended :** Submittal of the Draft Feasibility Study Addendum for Operable Unit (OU) 19, Site 44
3. **Length of extension/new deadline:** 90 days from December 14, 2014 to March 14, 2015.
4. **Good Cause**
 - Force Majeure
 - Another Parties failure
 - Dispute Resolution
 - Delay caused by extension granted for other deadline
 - Events or series of events mutually agreed to by the Parties
5. **Brief description/explanation of cause:**

Although the NAS Pensacola CY2015 SMP does not list the OU 19, Site 44 Feasibility Study Addendum on its schedule, the NAS Pensacola 2014 SMP specified that the Draft Feasibility Study Addendum for OU 19, Site 44 be submitted on February 16, 2014. Extension requests submitted in 2014 moved the approved submittal date to December 14, 2014. Prior to submittal, groundwater sampling and contaminant delineation was to be completed. Throughout CY 2014, the Navy continued assessment activities however the complete delineation of the groundwater plume has not been determined. However the Navy and regulatory agencies did not want to

postpone the Feasibility Study Addendum and site progress, therefore they decided to proceed with the Feasibility Study Addendum and incorporate the data in the document as it becomes available. Submittal of the Draft Feasibility Study Addendum has been further delayed to incorporate informal comments from the regulators including a request for inclusion of a "Preferred Alternative" section to the document and revisions to the ARARs tables for regulatory comments received on the NAS Pensacola OU 2 Feasibility Study Addendum.

As indicated above, the Draft Feasibility Study Addendum for OU 19, Site 44 has a revised submittal date of December 14, 2014. Based on delays due to pre-submittal incorporation of informal regulatory comments, the Navy requests a milestone schedule extension of 90 days with a proposed revised submittal date for the Draft Feasibility Study Addendum from December 14, 2014 to March 14, 2015. This schedule extension will also extend the milestone due dates for the Final Feasibility Study Addendum and future documents including the Proposed Plan, Record of Decision, and Remedial Design included in the NAS Pensacola CY2015 SMP. A revised Milestone Schedule that reflects the 90 day schedule extension is attached.

The 90 day extension will allow:

- Continued progress at the site but allow incorporation of the quarterly groundwater monitoring results to be incorporated into the Draft Feasibility Study Addendum.


IT IS SO AGREED

MARAJH
WHITTEMORE.PATTY.136266
5520

Digitally signed by MARAJH WHITTEMORE.PATTY.1362661520
DN: cn=US, o=U.S. Government, ou=DoD, ou=FE, ou=OSX,
cn=USARMC, cn=WHITTEMORE.PATTY.1362661520
Date: 2015.01.26 11:17:52 -0500

Patty Marajh – Whittemore
Remedial Project Manager
NAVFAC SE

Date



1/14/15
Date

Timely

Good Cause

David Grabka
Remedial Project Manager
Florida Department of Environmental Protection

Timothy R
Woolheater

Digitally signed by Timothy R Woolheater
DN: cn=Timothy R Woolheater, o=USEPA,
ou=MSF-FEB,
email=woolheater.tim@epa.gov, c=US
Date: 2015.01.26 11:37:04 -0500


Timely

Good Cause

Tim Woolheater
Remedial Project Manager
USEPA, Region 4

Date

NAS PENSACOLA
DOCUMENT GANTT CHART
 SMP 2015 - Revised OU 19, Site 44 Gantt Chart
 SMP Extension 2015-1 January 2015

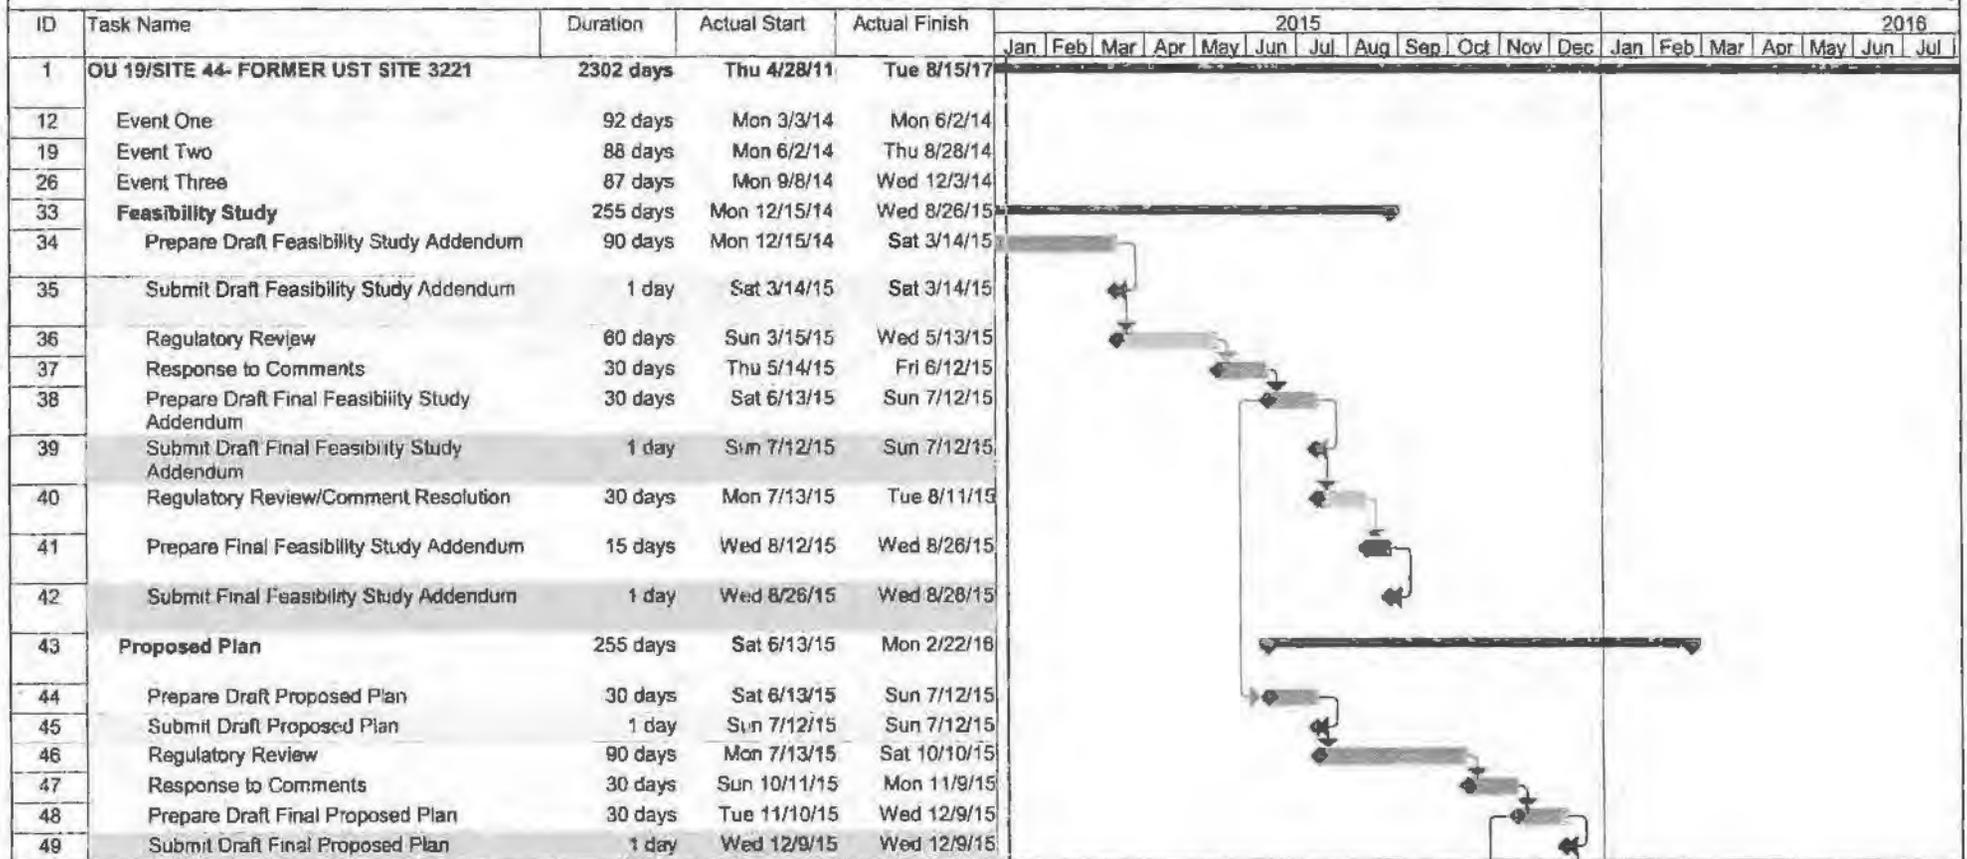

Blue block- Navy Green block- Regulators Red block- Approval	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Progress	
	External Tasks		Duration-only		Deadline	

